


Pre-Demo Planning Module — Gantt & Backlog

Demo Day: Tuesday, 2 June 2026.

The whole pre-demo period runs on **canned/sim data** (locked in PD-011) — zero live data, zero backend API, zero Profiling-handoff work is due before the demo. That post-demo work moves to June/July (see docs/PLANNING_MODULE_ROADMAP.md). The trade-off is deliberate: predictability and consistent demo-day UI behaviour over real-data realism.

Everything below maps 1:1 to the JIRA tickets in docs/JIRA_powerdime_import.csv .


Pre-Demo Stories (PD-001 → PD-019) + Demo Day (PD-020)

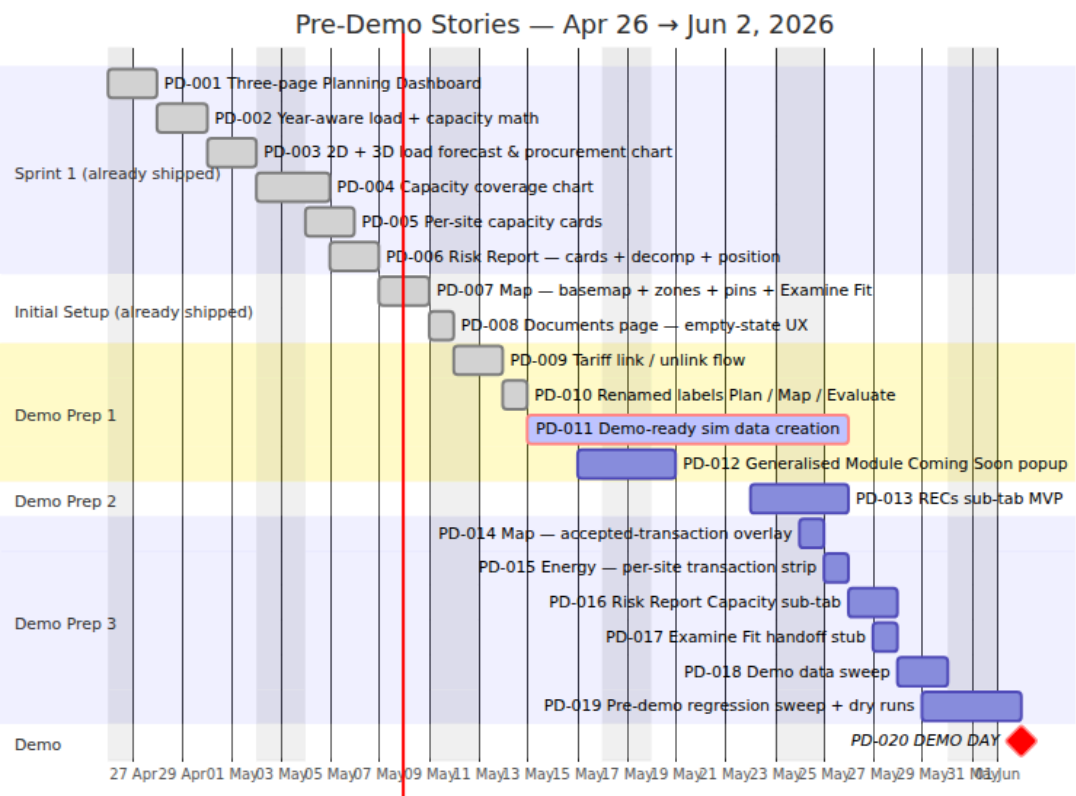

Wiring & Sync Test Sub-tasks (PD-068 → PD-094)

Every visible feature has a paired wiring & sync test that runs after its build Story is complete. The acceptance criterion is universal: **feature sync wiring completed end-to-end + sync testing completed with 0 errors and 0 unexpected results.**

Wiring & Sync Tests — May 25 → May 31, 2026

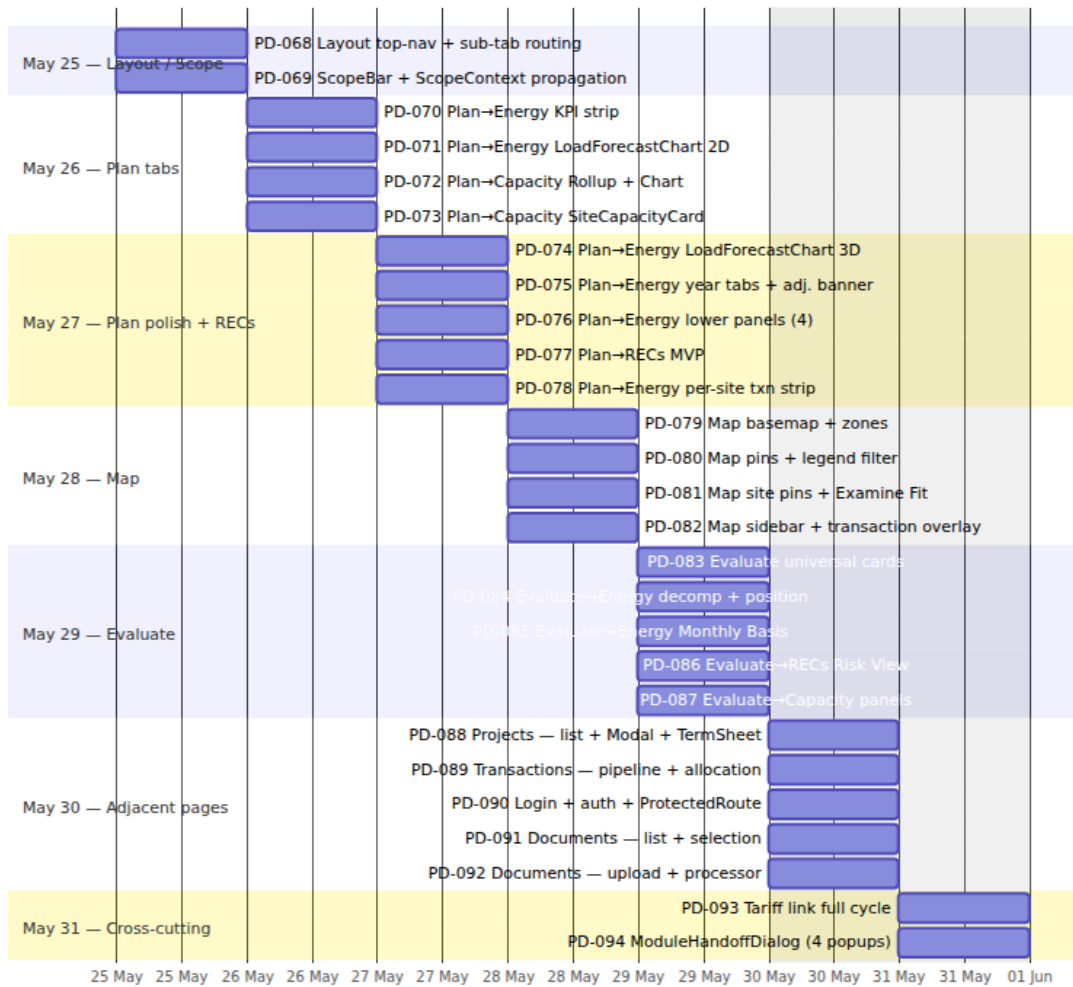

Story Topics + Their Sub-tasks

Sprint 1 — Already shipped

Story	Description	Wiring sub-tasks
PD-001 Three-page Planning Dashboard	Plan / Map / Evaluate routes, persistent scope header, Capacity / Energy / RECs sub-tab row, cross-page state preservation.	PD-068 (top-nav + sub-tabs), PD-069 (ScopeBar), PD-088 (Projects), PD-089 (Transactions), PD-090 (Login + auth)
PD-002 Year-aware load + capacity math	LoadAdjustment + CapacityByYear types, getEffectiveLoadAt + getSiteCapacityForYear helpers, single-site + aggregate paths. The Manassas	(math layer — covered by chart wiring tests below)

	+25% Jul 2027 demo bump propagates through every consumer.	
PD-003 2D + 3D load forecast & procurement chart	Plan→Energy chart: per-hour or per-month bars with teal baseload + amber peak tier shading, per-contract patterns, oblique ribbon 3D mode, over-hedge below y=0.	PD-070 (KPI strip), PD-071 (2D mode), PD-074 (3D ribbon), PD-075 (year tabs + adj. banner), PD-076 (lower panels)
PD-004 Capacity coverage chart	Plan→Capacity indigo capacity bar with per-source SVG patterns. Bar height steps year-over-year for documented expansions.	PD-072 (Rollup + Chart pipeline)
PD-005 Per-site capacity cards	Brownfield BRA panel + greenfield options table per site. View Document / Solicit RFQ / View BRA History dialogs.	PD-073 (SiteCapacityCard panels + dialogs)
PD-006 Risk Report — cards + decomp + Contracted Position	Evaluate page: 5 summary cards, 5-row risk decomposition table, per-site Contracted Position bars. Year-tab synchronises headline cards with chart.	PD-083 (universal cards), PD-084 (decomp + position), PD-085 (Monthly Basis), PD-086 (RECs Risk View), PD-087 (Capacity panels)

Initial Setup — Already shipped

Story	Description	Wiring sub-tasks
PD-007 Map — basemap, zones, pins, Examine Fit	OSM basemap, PJM zone overlay, project pins by gen type, buyer site pins, Examine Fit ribbon.	PD-079 (basemap + zones), PD-080 (pins + legend), PD-081 (site pins + Examine Fit)
PD-008 Documents page UX	Graceful empty state on backend failure (no scary red banner). Console diagnostic preserved for devs.	PD-091 (list + selection), PD-092 (upload + processor)

Demo Prep 1

Story	Description	Wiring sub-tasks
PD-009 Tariff link / unlink flow	View Document on Capacity card opens linked tariff or routes to Documents in selection mode. localStorage-persisted.	PD-093 (tariff link full cycle)
PD-010 Renamed labels — Plan / Map / Evaluate	User-facing rename: Forecast → Plan, Risk → Evaluate; Hedge Coverage → Contracted Coverage; Hedge Position → Contracted Position.	(label-only — covered by Layout wiring test PD-068)
PD-011 Demo-ready sim data	Lock the demo dataset as TypeScript constants under <code>src/data/</code> . 3 DOM sites with full profile, capacity expansions, mid-year load bumps,	(foundational — every wiring test below verifies the

creation IN FLIGHT	staggered contracts, BRA capacity sources, LMP basis bands, site financials. This is the foundation that lets the demo run with zero backend dependency.	sim data renders correctly)
PD-012 Generalised Module Coming Soon popup	Generalise ComingSoonDialog into a top-level ModuleHandoffDialog with module name + completion target + payload preview. Wired to every CTA that crosses an unfinished module boundary.	PD-094 (4-popup set: Solicit RFQ / Examine Fit / View BRA / Accept Txn)

Demo Prep 2

Story	Description	Wiring sub-tasks
PD-013 RECs sub-tab MVP	Per-site target % + current REC coverage % + gap MWh + annual ESG cost. Annual matching only — full time-matching is post-demo. Plan→RECs and Map→RECs both render real content (not "coming soon").	PD-077 (Plan→RECs MVP), PD-086 (Evaluate→RECs Risk View)

Demo Prep 3

Story	Description	Wiring sub-tasks
PD-014 Map — accepted-transaction overlay	Connector lines from each contracted project pin to the buyer site(s) it hedges, one per perSiteMw entry. Hover popup names the contract, MW, term.	PD-082 (sidebar + fly-to + transaction overlay)
PD-015 Energy — per-site transaction summary strip	One-line strip per site listing every accepted transaction (project · MW · shape · term). Sits between KPI strip and load chart.	PD-078 (per-site txn strip)
PD-016 Risk Report Capacity sub-tab	Build out the scaffolded panel: Capacity-cost summary card, BRA volatility band, Fixed-term-vs-pass-through comparison.	PD-087 (Capacity panels)
PD-017 Examine Fit handoff stub	Wire the Map's Examine Fit primary CTA to ModuleHandoffDialog with a documented Contracting payload schema visible on hover.	(handoff — covered by PD-094 popup wiring test)
PD-018 Demo data sweep	Lock the demo storyline. Confirm same data renders identically before / after migration to live (post-demo). Demo script written referencing concrete numbers.	(data lock — covered by regression sweep PD-019)
PD-019 Pre-demo regression sweep + dry runs	Smoke-test full Planning Module against locked sim fixtures (PD-011): scope changes, year tabs, site (de)selection, contract term boundaries, mid-year	(top-level regression — wraps every wiring test)

	bump, capacity step-ups, over-hedge rendering, every popup fires. Two clean dry-runs.	
--	---	--

Demo Day

Story	Description
PD-020 — DEMO DAY	Live demo. Walk Pillars 1, 2, 3 in order. Demonstrate scope/duration control, 4D math through year tabs, Map filter + accepted-transaction overlay, Risk Report P10/P50/P90, Solicit RFQ → completion-date popup.

What's NOT in this Phase (intentional punts)

These were on earlier versions of this Gantt and have moved to post-demo (June/July) so the pre-demo period stays predictable:

- **PD-023** DB Foundation schema — moved to **June 8-15**
- **PD-025** Backend API v1 — moved to **June 15 - July 3**
- **PD-033** Profiling Module → Planning Module live data interface — moved to **July 6-24**
- **PD-040** Demo-mode feature flag — moved to **July 27-31**

The full post-demo backlog (Jun 5 → Dec 31, including Contracting Module integration, 3-ISO live data ingestion, ML risk engine, and beta customer pilots) is in `docs/PLANNING_MODULE_ROADMAP.md` and as JIRA-importable rows in `docs/JIRA_powerdime_import.csv`.

Pre-Demo Counts

Sprint	Stories	Sub-tasks
Sprint 1	6	0
Initial Setup	2	0
Demo Prep 1	4	0
Demo Prep 2	1	0
Demo Prep 3	6	27
Total before Demo Day	19	27
Demo Day milestone	1	—
